Art Gallery Exhibition Management System

Project Planning: Task Identification, Activity Table and Gantt Chart

1. Task Identification

The project is divided into main tasks, and each task is divided into smaller subtasks. Example task:

Task Information	Details
Name of Task	Requirements Analysis
Start Date	19-10-2026
End Date	21-10-2026
Person assigned to task	Abdelrhman Emad
Priority	High
Resources Needed	Microsoft Word, Draw.io
Estimated Time	12 Hours
Actual Time	10 Hours

2. Activity Table

Activity	Description	Predecessors	Duration (days)
A	Requirements Analysis	-	3
B	Database Design	A	4
C	User Interface Design	A	2
D	System Implementation and Testing	B, C	6

3. Solution (Earliest Start / Finish)

Activity	Start	Finish	Explanation
A	0	3	No predecessors, starts at day 0
B	3	7	Starts after A finishes (3 + 4)
C	3	5	Starts after A, runs in parallel with B (3 + 2)
D	7	13	Waits for B and C; B finishes later, so D starts at 7 (7 + 6)

Critical path: A to B to D | **Total project duration:** 13 days. Activity C has 2 days of slack because it finishes at day 5 while D cannot start before day 7.
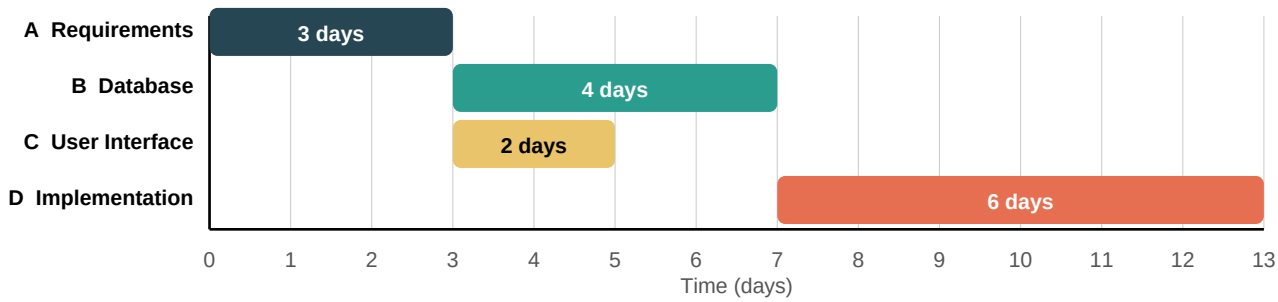
4. Gantt Chart
